

Greenfield Connections

Performance & consultation report

Q4 2025



1. Actions

Actions from last meeting

Actions				
#	Who	Description	Date due	Status
2.4	SR	<u>Make contact with JT and TI (ALDE)</u> , regarding traffic signal, public light projects and in progress tie-in initiative <i>A tentative arrangement has been made for JL and TI to attend a trial site with Powercor in 2025</i>	Q4 2025	Open
2.5	JT	Share contacts relevant to traffic signal and public light projects	Q3 2025	Open

2. Performance

Quarter 4 2025

Q4 2025 Performance | CitiPower/Powercor

Summary

- It has been another steady quarter (Q4) in 2025 with all performance metrics above target except average days to tie in, which has reduced on average by 10 days in Q4, similar to Q3 at 39 days and as-built review target slightly under at 68% on a target of 70%.
- Masterplan review was just above target in Q4, 83% within 10 days (target 80%), and the average time to complete remained positive to target at 8 days.
- Design review and field audit results for Q4 both remain favourable to target in Q3, with design review completed on average in 9 days and 91% of field audits completed in 6 days.
- Average days to tie in has reduced on average by 10 days in Q3 and now Q4 to an average of 39 days and 96% of tie ins have been completed by the agreed date.
- Powercor's strategic project to improve tie-in timeframes is well under way with a progress update to follow shortly after this metric update.

2025 Performance | CitiPower/Powercor

Process step	Measure	Full year 2024	Q2 2025	Q3 2025	Q4 2025	Status 2025
Masterplan reviewed	80% in 10 days	Average 6 days 88% within 10 days (362 completed)	Average 6 days 77% within 10 days (84 completed)	Average 7 days 81% within 10 days (96 completed)	Average 8 days 83% within 10 days (83 completed)	●
Design reviewed	Average: 15 days	Average 10.3 days (716 completed)	Average 8 days (215 completed)	Average 8 days (248 completed)	Average 9 days (208 completed)	●
As built plan reviewed	70% in 5 days	67% within 5 days (1281 completed)	68% within 5 days (277 completed)	70% within 5 days (303 completed)	68% within 5 days (252 completed)	●
	Average: 8 days	Average 4.4 days	Average 4 days	Average 4 days	Average 4.3 days	●
Audit complete	70% in 6 days	91% within 6 days	78% within 6 days	90% within 6 days	91% within 6 days	●
Certificate of practical completion	95% in 5 days	90% within 5 days (528 completed)	98% within 5 days (83 completed)	100% within 5 days (98 completed)	97% within 5 days (113 completed)	●
Time to tie in	Average: 20 days	47 days	49 days	39 days	39 days	●
	>95% by agreed date	90%	96%	97%	96%	●

2025 Performance | United Energy

Summary

- Performance across all areas in UE are at 100% with, 4 URD projects received YTD in 2025, all metrics are currently meeting or exceeding target.


2025 Performance | United Energy

Process step	Measure	Target	Full year 2024	Q2 2025	Q3 2025	Q4 2025	Status 2025
Offer issued	% completed within time frame	20 days	100% (6 URD offers in 2024 – issued in 12 days)	100% (3 URD design reviews in Q2 2025 – issued in 13 days)	Zero applications	100% (1 URD design reviews in Q4 2025 – issued in 5 days)	
Masterplan review	% completed within time frame	10 days	Not applicable	Not applicable	Zero applications	Not applicable	
Design review	% completed within time frame	20 days	100% (5 URD design reviews in 2024 – issued in 15 days)	Not applicable	Zero applications	Current stage	
Authority to construct	% completed within time frame	10 days	100% (7 ACC issued in Q4 2024 – reviewed at average 3 days)	100% (3 ACC issued in Q2 2025 at average 1 days)	Zero applications	Future stage to be commenced	
Authority to commission	% completed within time frame	10 days	100% (6 ACCC issued in Q4 2024 – reviewed at average 3 days)	100% (1 ACC issued in Q2 2025 at average 1 days)	Zero applications	Future stage to be commence	

2a. VPN audit breakdown by type

Sam Reidy

VPN Audit breakdown | Volumes Q4 2024 & 2025 YTD

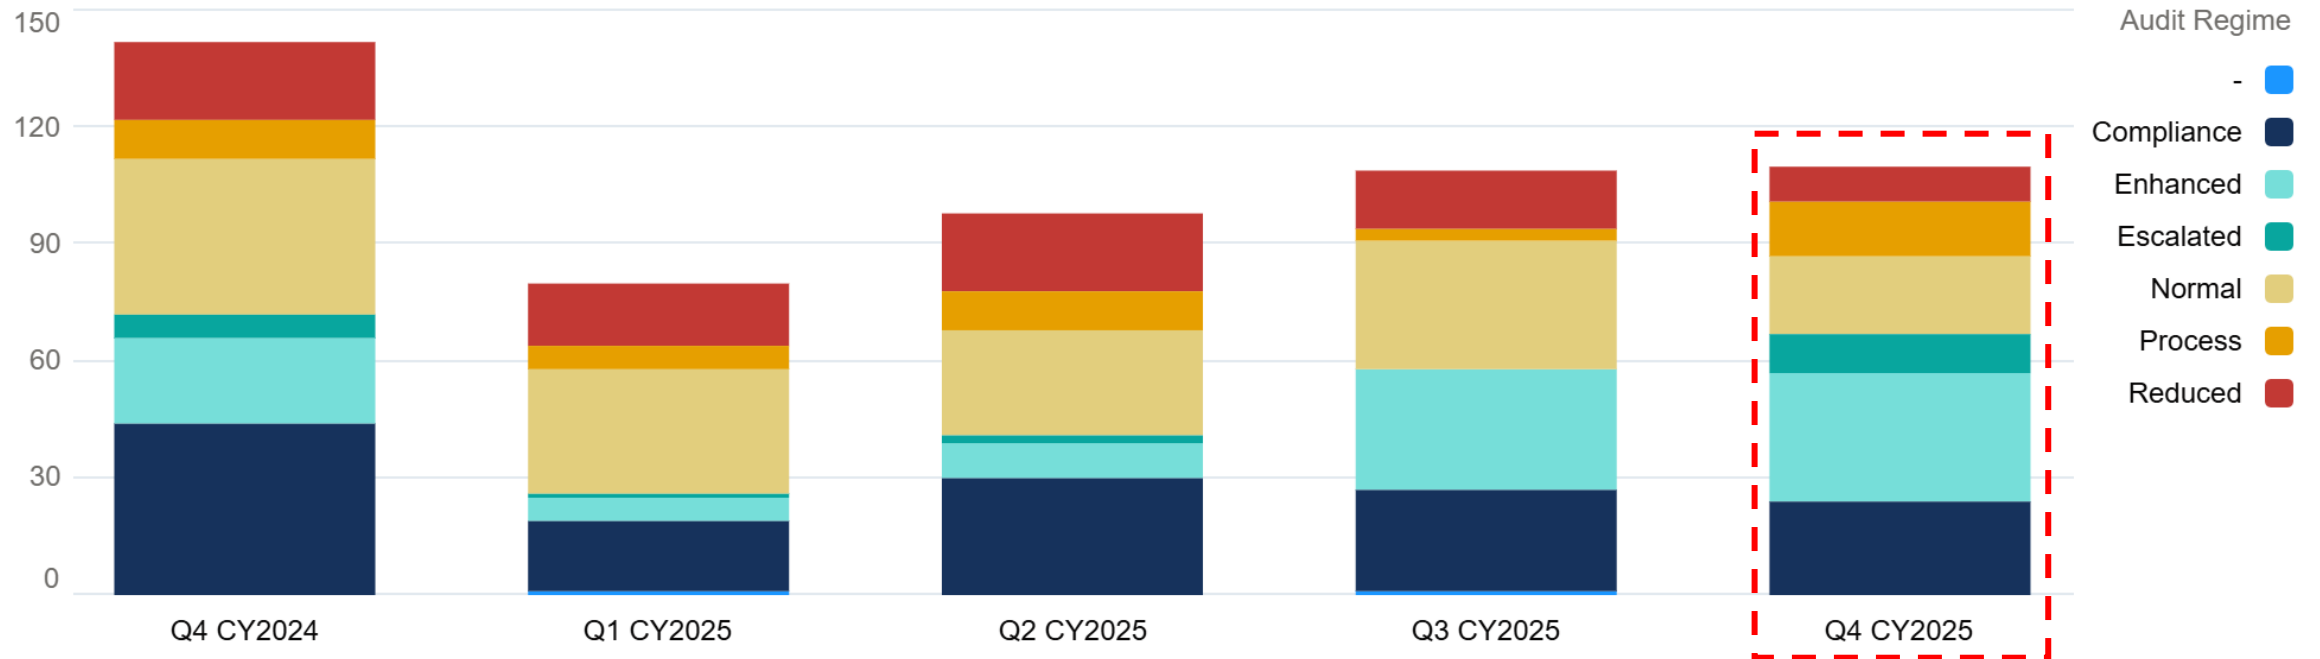

- YTD audit volumes have trended down compared to 2024.
- The number of enhanced and escalated audits in Q4 has increased dramatically on account of the recent downward movement of 'volume' contractors in the contractor ratings. This trend likely to start to trend more favorably in Q1 2026.
- We do however continue to complete a significant amount of audits from the desk signified by the dark blue, red and orange.

3. Strategic projects update

Sam Reidy

Faster Tie-In

Progress update

2nd March 2026






Contents

- 1. Proposed Process
- 2. Timeline / Rollout

Future Process

Express contestable works tie in

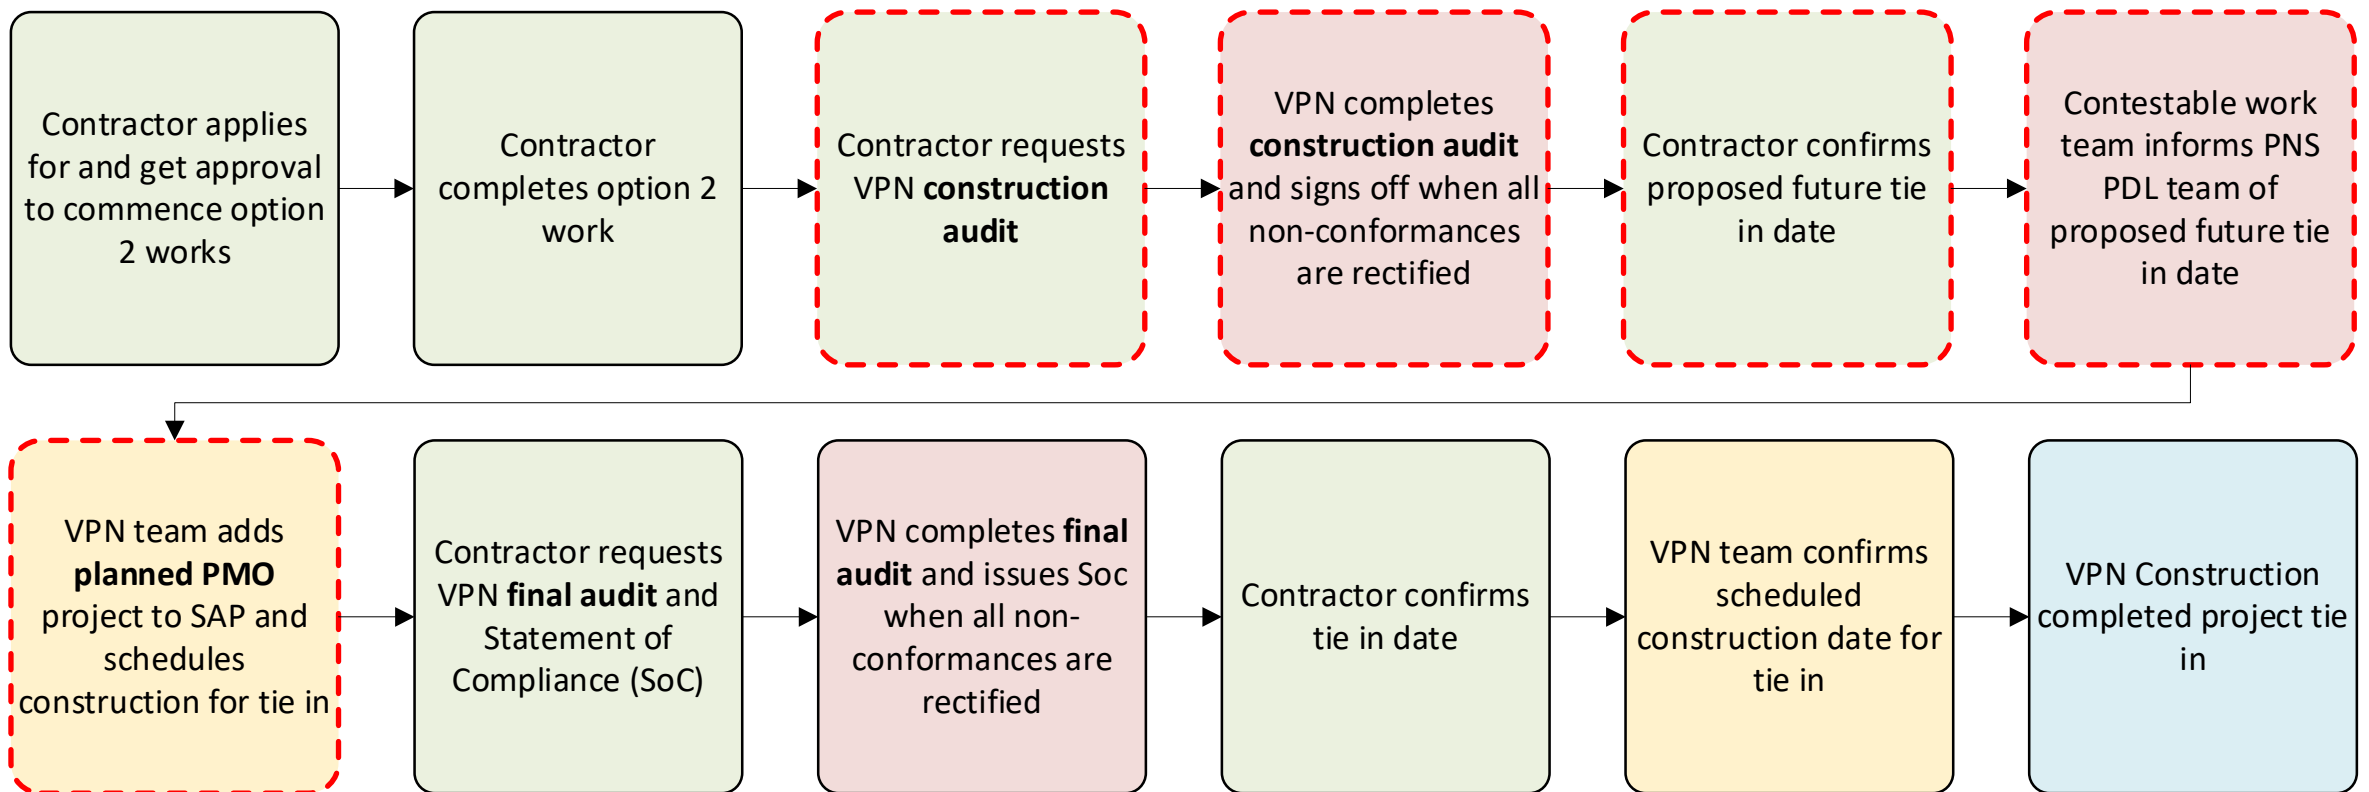

Faster Tie-In

System updates, key communications and industry 'Go Live'

Ongoing trial via 'workaround' initiated with industry partners, running parallel

